
\*

Sprint #9 Remaining Time Estimate •

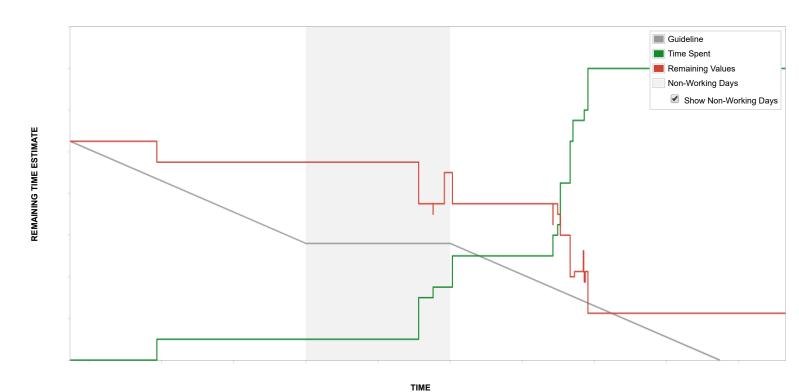

Date	Issue	Event Type	Event Detail	Time Spent			Remaining Time Estimate			
				Inc.	Dec.	Sum	Inc.	Dec.	Remaining	
21/May/19 5:40	MARK-	Sprint start		-			4h			
PM	140			-			2h			
	MARK-			-			2h			
	150			-			5h			
	MARK-			-			-			
	168			-			0			
	MARK-			-			4h			
	175			-			1h			
	MARK-			-			2h			
	185			-			1h			
	MARK-			-			-			
	195			-			-			
	MARK-					0			21h	
	197									
	MARK- 198									
	MARK-									
	199									
	MARK-									
	202									
	MARK-									
	203									
	MARK-									
	204									
22/May/19 10:28 PM	MARK- 199	Work logged	2h logged, Remaining Time Estimate changed from 2h to 0	2h		2h		2h	19h	
22/May/19 10:29 PM	MARK- 199	Issue state change	Issue completed	0		2h	0		19h	
26/May/19 1:31 PM	MARK- 197	Work logged	4h logged, Remaining Time Estimate changed from 4h to 0	4h		6h		4h	15h	

		Event Type	Event Detail	Time Spent		Remaining Time Estimate			
Date	Issue			Inc.	Dec.	Sum	Inc.	Dec.	Remaining
26/May/19 5:31 PM	MARK- 197	Issue state change	Issue completed	0		6h	0		15h
26/May/19 6:00 PM	MARK- 211	Scope change	Issue added to sprint	0		6h	0		15h
26/May/19 6:19 PM	MARK- 211	Work logged	1h logged, Remaining Time Estimate changed from 0 to -1h Backdated event, recorded at 26/May/19 6:20 PM	1h		7h		1h	14h
	MARK- 211	RTE change	Remaining Time Estimate changed from -1h to 0 Includes -3,600 backdated to 26/May/19 6:19 PM, recorded at 26/May/19 6:20 PM	0		7h	1h		15h
	MARK- 211	Issue state change	Issue completed	0		7h	0		15h
26/May/19 9:52 PM	MARK- 212	Scope change	Issue added to sprint	0		7h	0		15h
26/May/19 9:55 PM	MARK- 212	Issue state change	Issue completed	0		7h	0		15h
26/May/19 10:03 PM	MARK- 106	Scope change	Issue added to sprint	0		7h	0		15h
	MARK- 106	RTE change	Remaining Time Estimate changed from 0 to 3h	0		7h	3h		18h
27/May/19 12:44 AM	MARK- 106	Work logged	3h logged, Remaining Time Estimate changed from 3h to 0	3h		10h		3h	15h
27/May/19 12:45 AM	MARK- 106	Issue state change	Issue completed	0		10h	0		15h
28/May/19 10:10 AM	MARK- 150	Work logged	2h logged, Remaining Time Estimate changed from 2h to 0	2h		12h		2h	13h
	MARK- 150	Issue state change	Issue completed	0		12h	0		13h
28/May/19 10:12 AM	MARK- 185	RTE change	Remaining Time Estimate changed from 0 to 2h	0		12h	2h		15h
	MARK- 185	Issue state change	Issue completed	0		12h	0		15h
28/May/19 11:44 AM	MARK- 185	Work logged	1h logged, Remaining Time Estimate changed from 2h to 1h	1h		13h		1h	14h
28/May/19 12:37 PM	MARK- 168	Work logged	4h logged, Remaining Time Estimate changed from 2h to 0	4h		17h		2h	12h
28/May/19 12:38 PM	MARK- 168	Issue state change	Issue completed	0		17h	0		12h
28/May/19 3:53 PM	MARK- 175	Work logged	4h logged, Remaining Time Estimate changed from 5h to 1h	4h		21h		4h	8h
	MARK- 175	Issue state change	Issue completed	0		21h	0		8h
28/May/19 4:49 PM	MARK- 106	Work logged	2h logged, Remaining Time Estimate changed from 0 to 0	2h		23h	0		8h
28/May/19 5:19 PM	MARK- 215	Scope change	Issue added to sprint	0		23h	0		8h
28/May/19 5:20 PM	MARK- 215	Issue state change	Issue completed	0		23h	0		8h
	MARK- 215	RTE change	Remaining Time Estimate changed from 0 to 0.5h	0		23h	0.5h		8.5h
28/May/19 8:14 PM	MARK- 216	Scope change	Issue added to sprint	0		23h	0		8.5h

Date	Issue	Event Type		Time Spe <u>Inc. Dec.</u>	ent Remaining Time Estimate				
			Event Detail		Dec.	Sum	Inc.	Dec.	Remaining
	MARK- 216	RTE change	Remaining Time Estimate changed from 0 to 2h	0		23h	2h		10.5h
28/May/19 8:24 PM	MARK- 216	Scope change	Issue removed from sprint	0		23h		2h	8.5h
28/May/19 8:34 PM	MARK- 198	Work logged	1h logged, Remaining Time Estimate changed from 1h to 0	1h		24h		1h	7.5h
28/May/19 8:55 PM	MARK- 216	Scope change	Issue added to sprint	0		24h	1h		8.5h
	MARK- 216	Issue state change	Issue completed	0		24h	0		8.5h
28/May/19 9:38 PM	MARK- 203	Issue state change	Issue completed	0		24h	0		8.5h
28/May/19 9:48 PM	MARK- 140	Work logged	4h logged, Remaining Time Estimate changed from 4h to 0	4h		28h		4h	4.5h
29/May/19 1:25 PM	MARK- 204	Issue state change	Issue completed	0		28h	0		4.5h
29/May/19 1:26 PM	MARK- 202	Issue state change	Issue completed	0		28h	0		4.5h
29/May/19 8:34 PM	MARK- 198	Issue state change	Issue completed	0		28h	0		4.5h
29/May/19 8:37 PM	MARK- 140	Issue state change	Issue completed	0		28h	0		4.5h
